

Tech Talks South Tyrol

Our Style Of Project Management

Fixed Time



Fixed Time

Fixed Scope

User Stories



User Stories

Milestone

Story Points




Story Points



Hours


Milestone Lifecycle

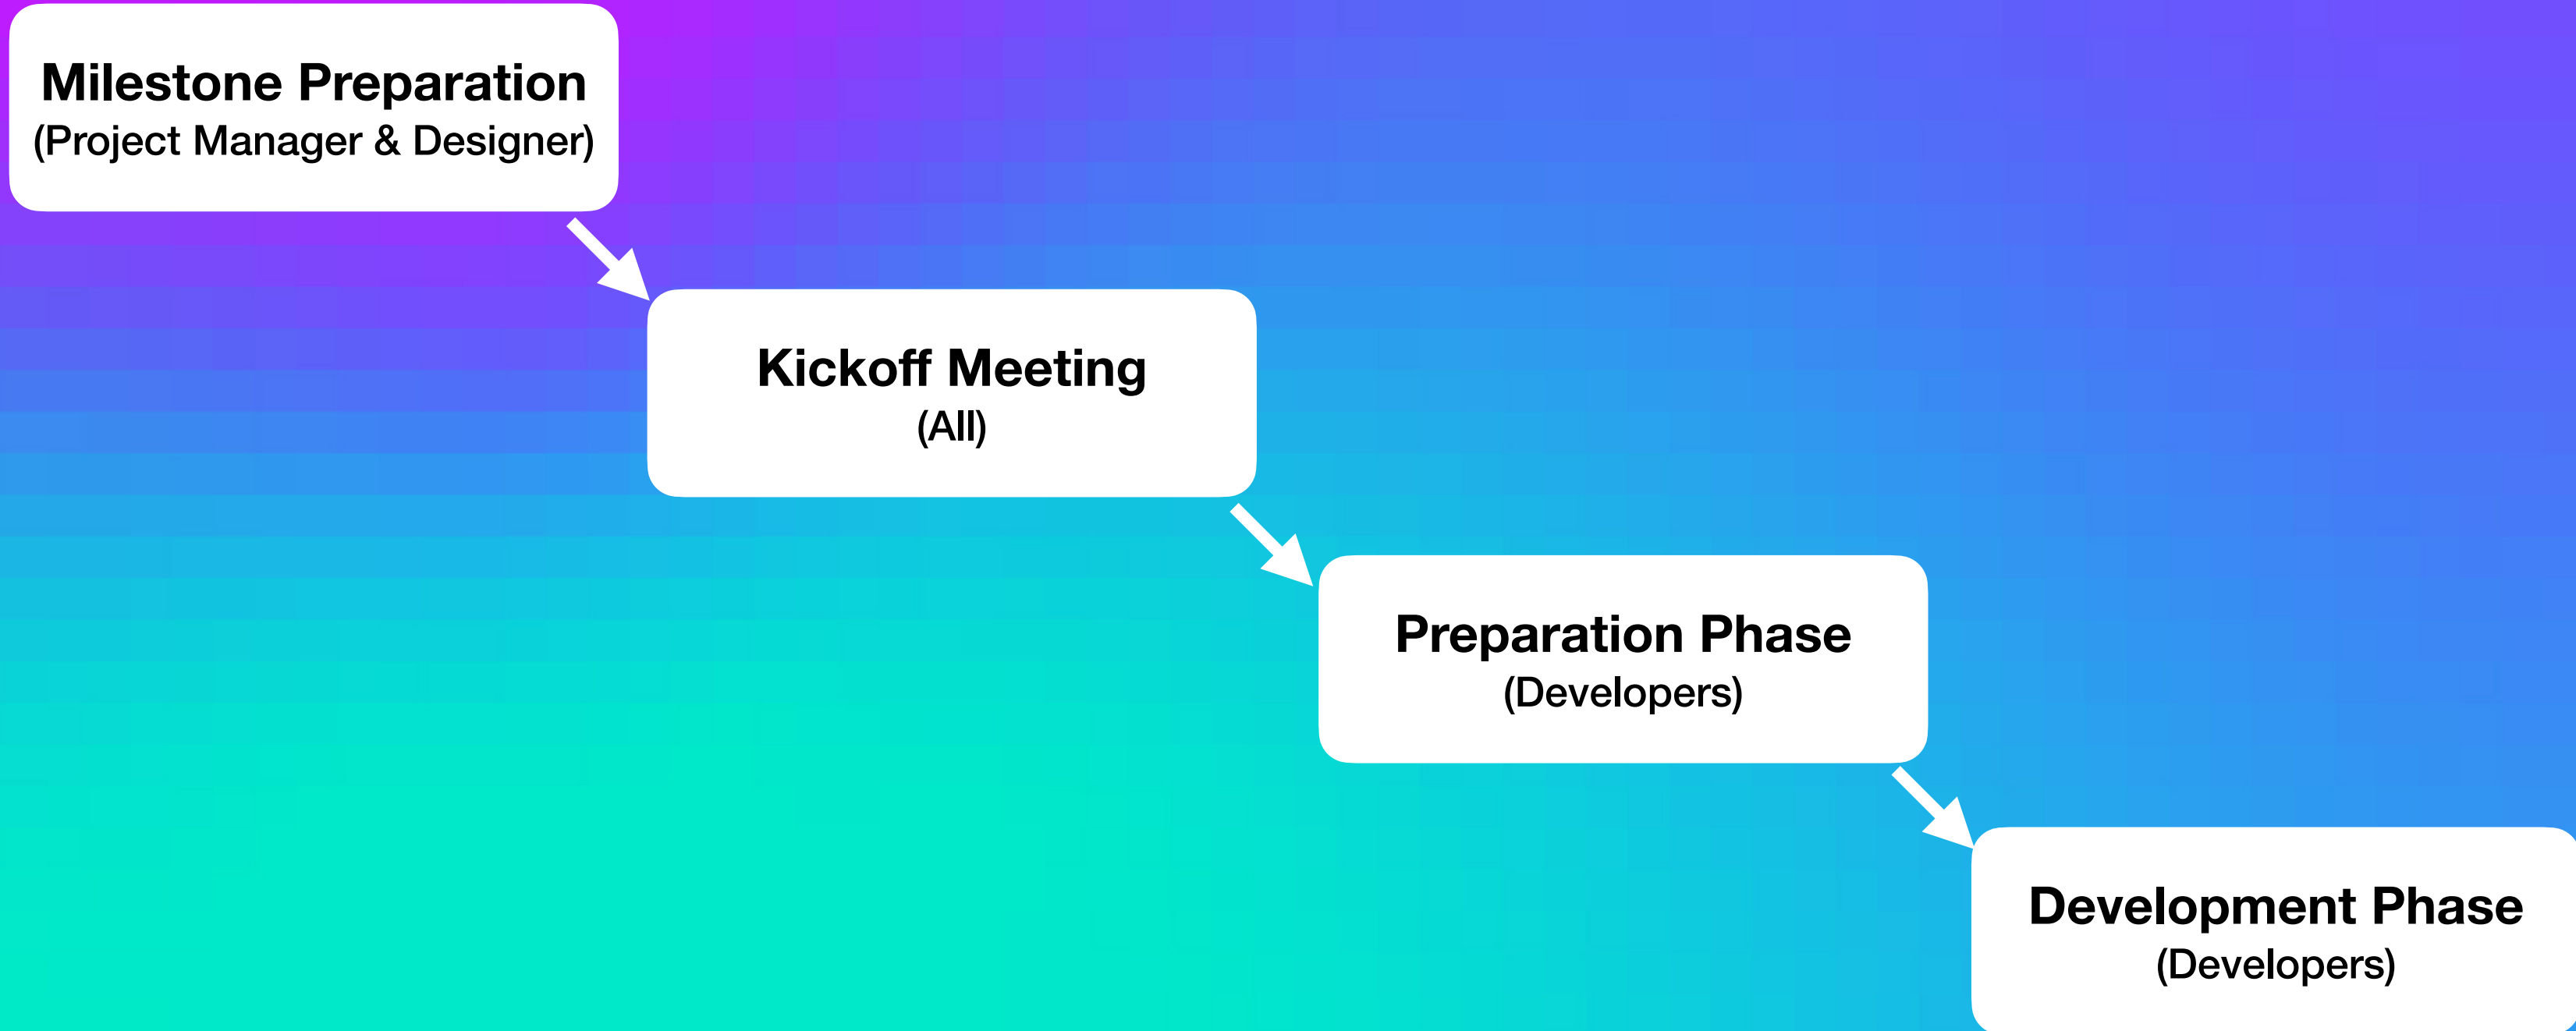

Kickoff Meeting

- The project manager presents the milestone
- A milestone contains a logical set of tasks
- The milestone definition is written down in a Notion document and designed in Figma
- The developers can ask questions if something is not clear

Milestone Lifecycle

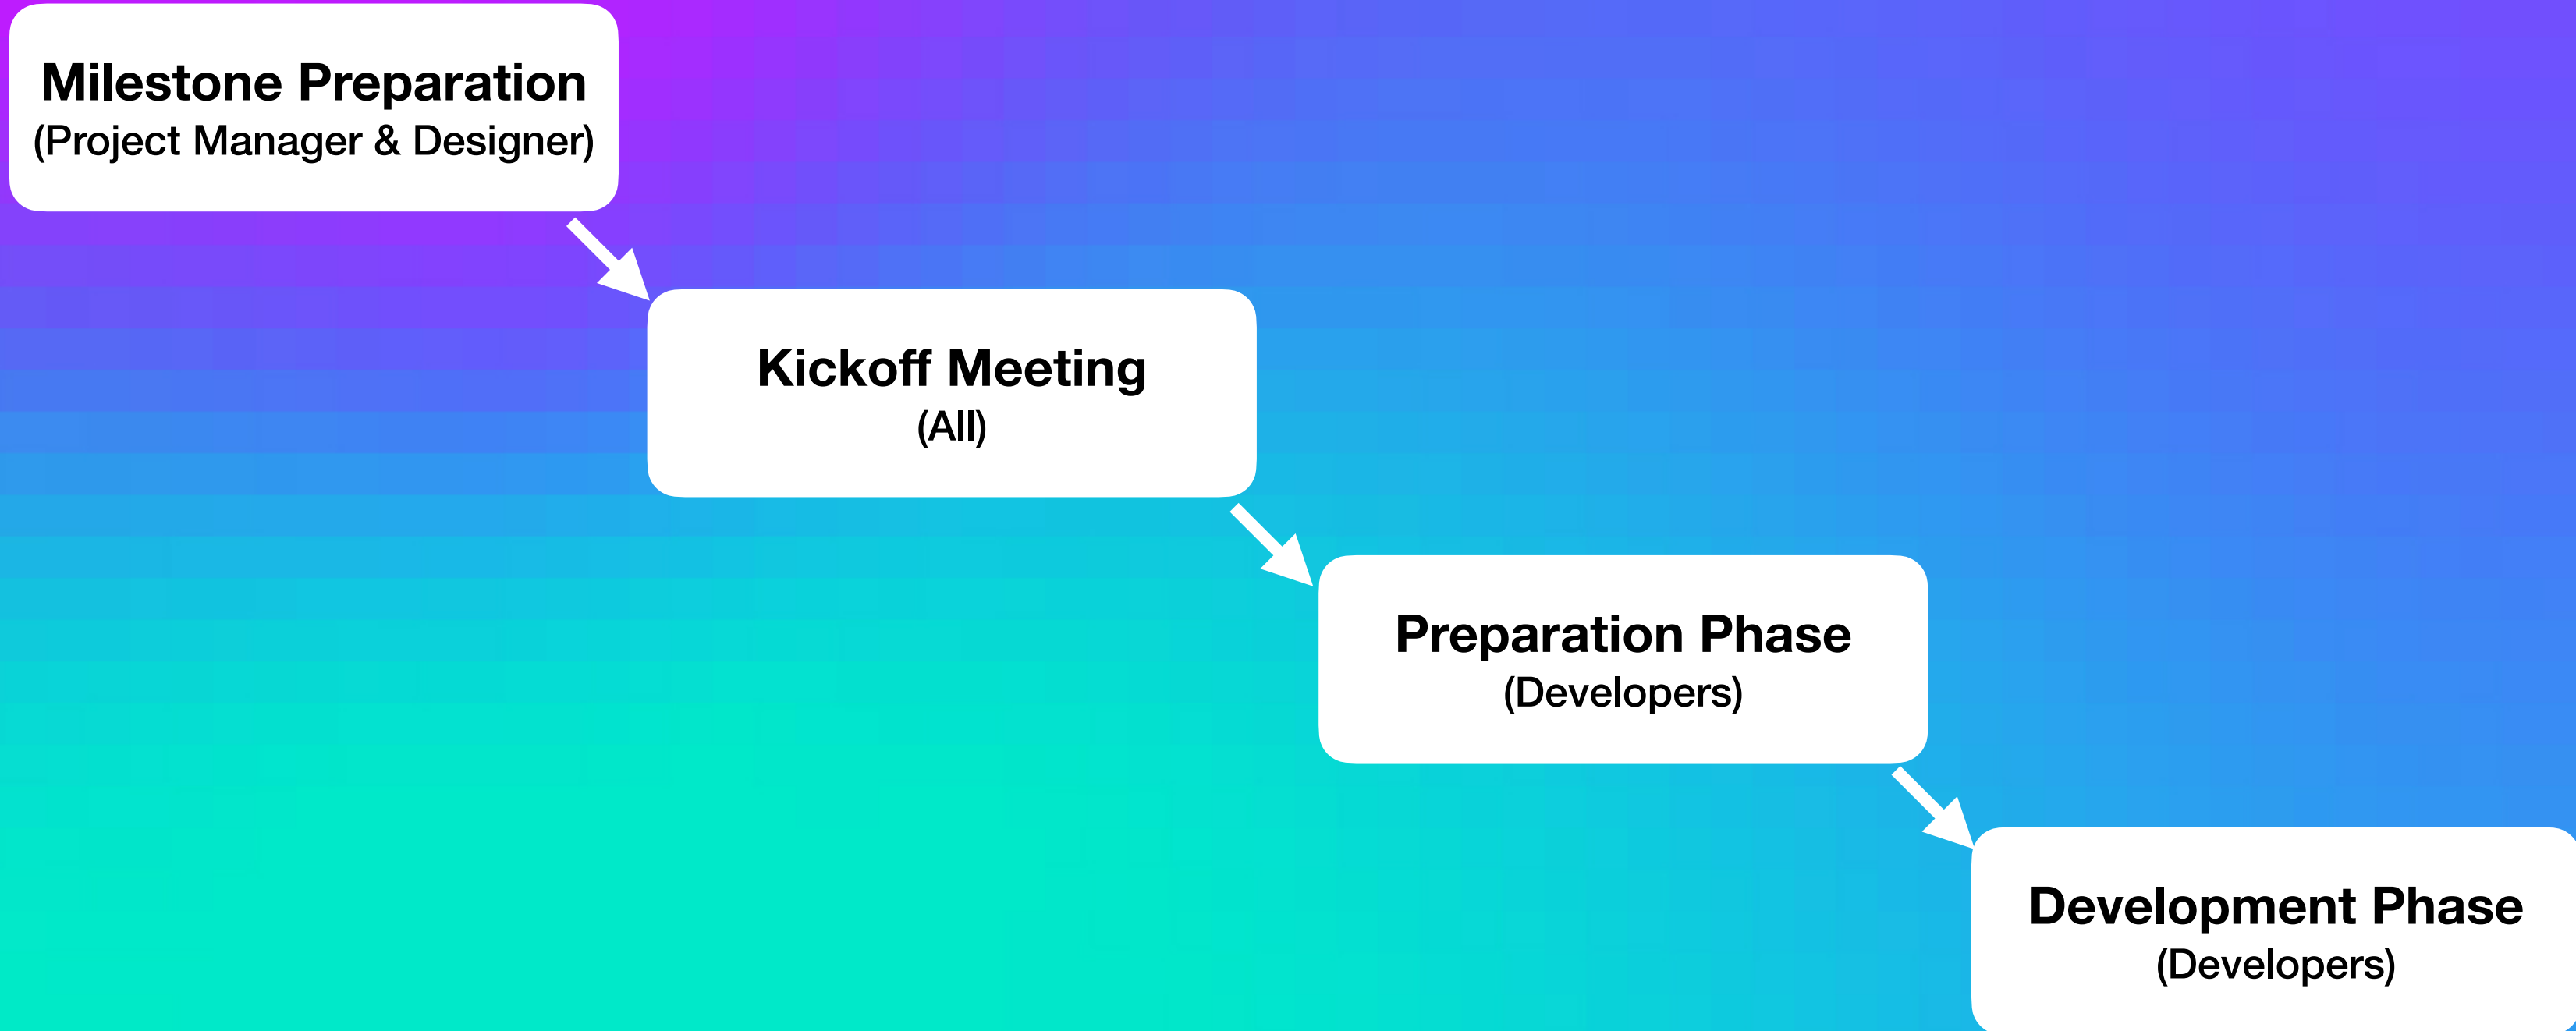


Preparation Phase

- The team elaborates the architecture
- The team creates tickets
- The team estimates the effort in hours
- This part is already part of the milestone

=>After a couple of days all will come together to discuss the estimation and the different architecture decisions

Milestone Lifecycle

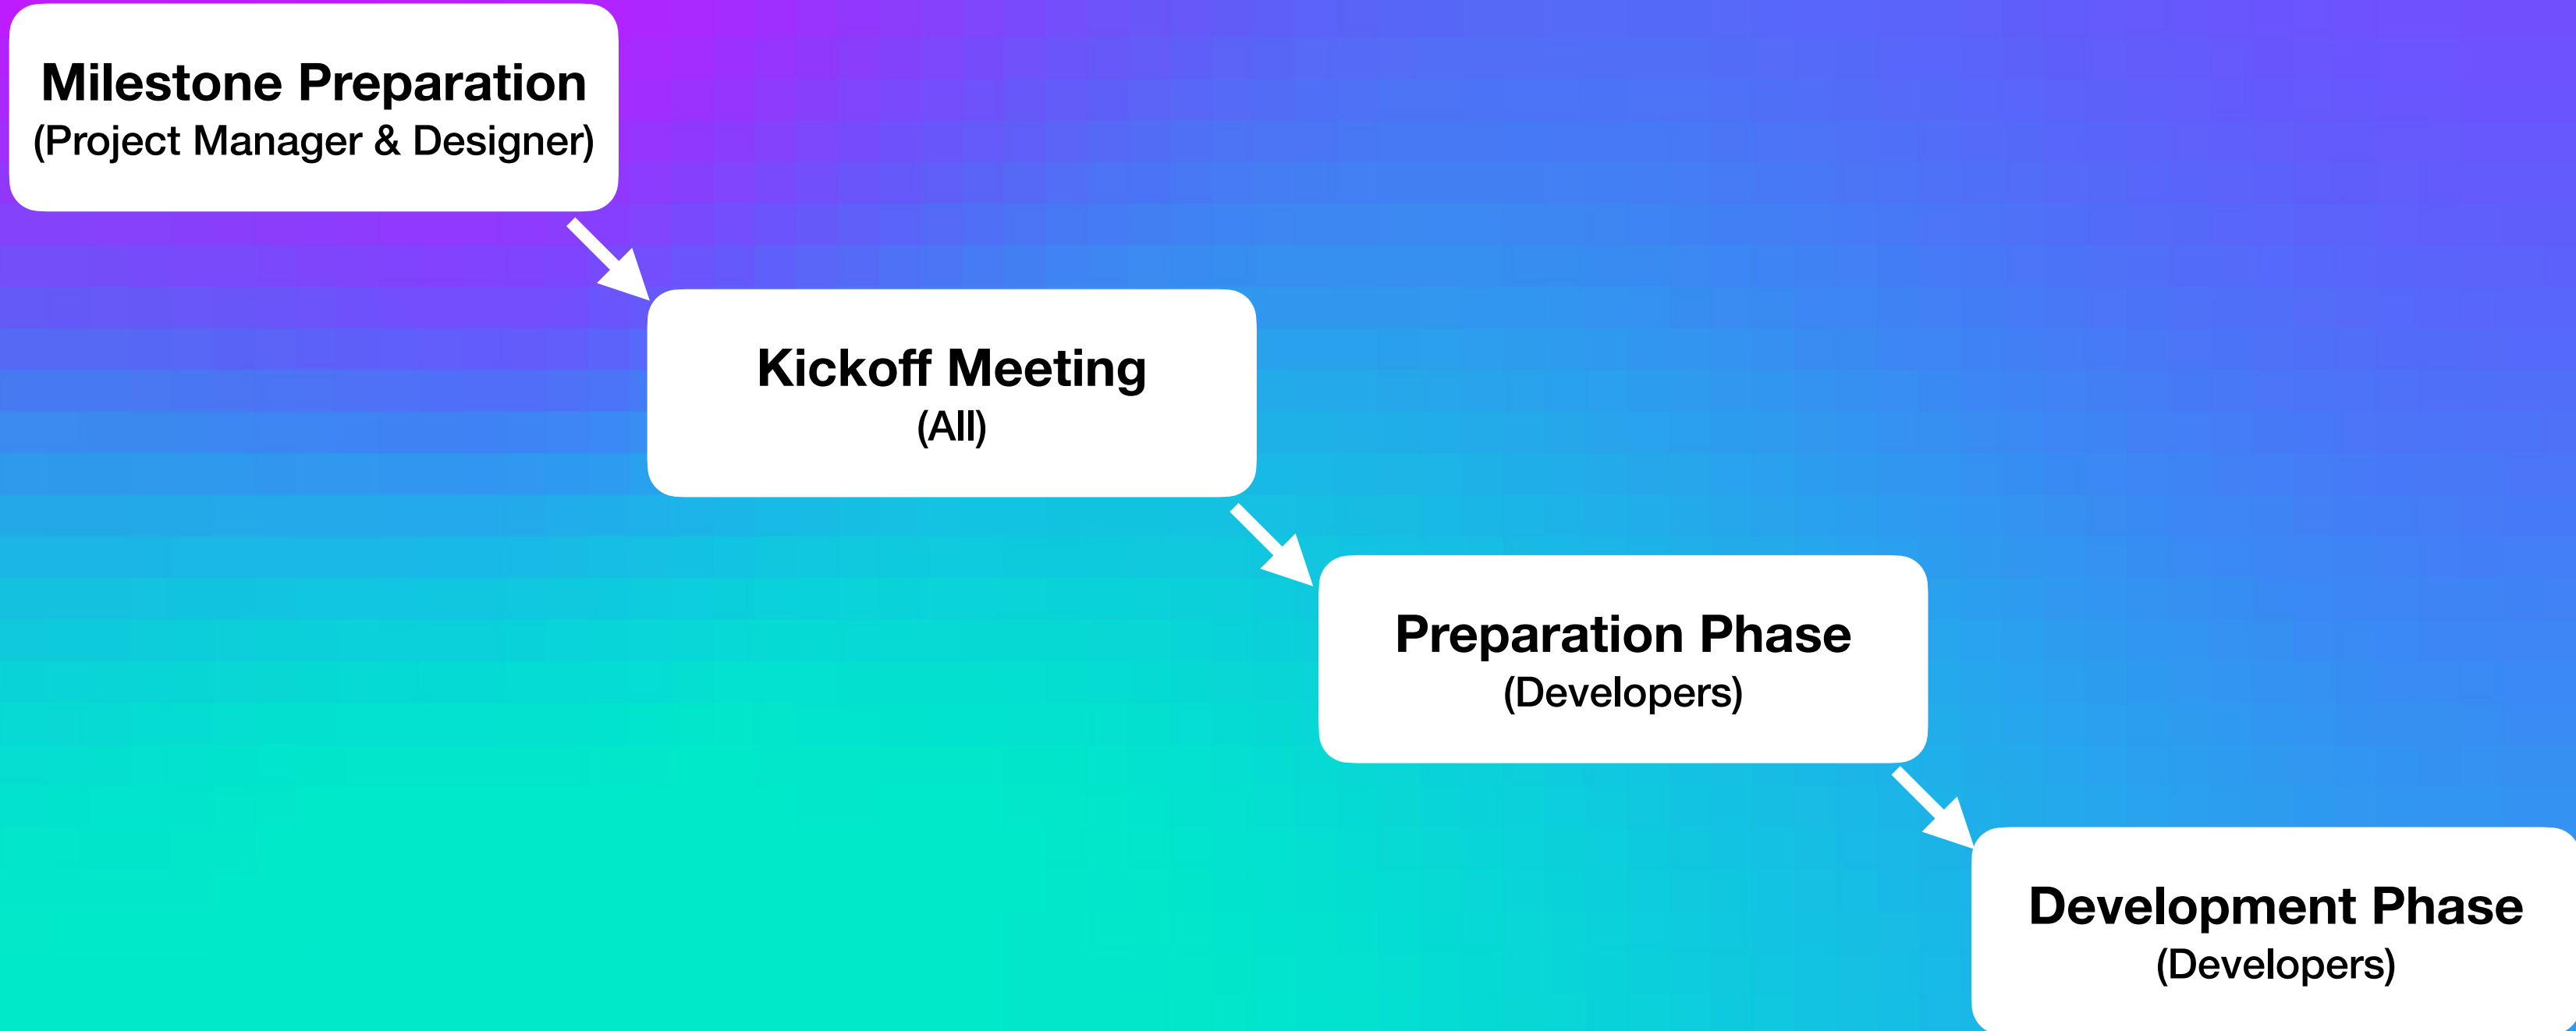

Development Phase

- Tickets are organized in a Kanban style
- Daily check ins with a standup
- Weekly alignment meetings to check the status of the milestone
- Weekly status updates about the current worked hours

=>After the milestone is completed, everyone gets together to reflect the milestone.

Weekly Planning

- A very high level plan for everyone for the next week
- Defined every Friday by the project managers
- We try to eliminate distractions and only allow someone to work on one project
- Gives us possibility to plan bug fixes

- Possibility to introduce new technologies, architectures and much more
 - Controlled and transparent way
 - Documented also for new employees
-
- Title
 - Author
 - Motivation
 - Proposed Solution
 - Drawbacks
 - Discussion Notes

Thank you.

AboutBits

About Bits GmbH
Färbergasse 12
I-39043 Klausen

[+39 338 6387751](tel:+393386387751)
info@aboutbits.it
www.aboutbits.it
